

REPORT DOCUMENTATION PAGE

Public reporting burden for this collection of information is estimated to average 1 hour per response, including the time for reviewing instructions, searching existing data sources, gathering and maintaining the data needed, and completing and reviewing the collection of information. Send comments regarding this burden estimate or any other aspect of this collection of information, including suggestions for reducing this burden, to Department of Defense, Washington Headquarters Services, Directorate for Information Operations and Reports, 1215 Jefferson Davis Highway, Suite 1204, Arlington VA 22202-4302, and to the Office of Management and Budget, Paperwork Project Director, Washington, DC 20503.

1. AGENCY USE ONLY (Leave Blank)		2. REPORT DATE Apr-07-00	3. REPORT TYPE AND DATES COVERED Monthly Progress Report Mar 1, 2000 - Mar 31, 2000
4. TITLE AND SUBTITLE Monthly Progress Report Wrist Interactive Device for Wearable PC		5. FUNDING NUMBERS Contract N00421-97-C-1293	
6. AUTHOR(S) Paolo Dini			
7. PERFORMING ORGANIZATION NAME(S) AND ADDRESS(ES) ViA Inc. 12550 West Frontage Rd. Burnsville, MN 55337		8. PERFORMING ORGANIZATION REPORT NUMBER	
9. SPONSORING/MONITORING AGENCY NAME(S) & ADDRESS(ES) Charles D. Caposell Code 4.0T Naval Air Systems Command Building 2185, Ste 1190 22347 Cedar Point Rd. Unit #6 Patuxent River, MD 20670-1161		10. SPONSORING/MONITORING AGENCY REPORT NUMBER	
11. SUPPLEMENTARY NOTES			
12a. DISTRIBUTION/AVAILABILITY STATEMENT Distribution A		12b. DISTRIBUTION CODE	
13. ABSTRACT (Maximum 200 words)			
14. SUBJECT TERMS		15. NUMBER OF PAGES	
		16. PRICE CODE	
17. SECURITY CLASSIFICATION OF REPORT Unclassified	18. SECURITY CLASSIFICATION OF THIS PAGE Unclassified	19. SECURITY CLASSIFICATION OF ABSTRACT Unclassified	
20. LIMITATION OF ABSTRACT			

**Contractor's Progress, Status and Management Report --
Monthly Progress Report**

**Period Covered by the Report
1 March through 31 March 2000**

Date of Report: 7 April 2000

Wrist Interactive Device for Wearable PC
SBIR Phase II Topic N95-137
Contract No. N00421-97-C-1293
Dollar Value \$1,708,653

ViA Inc.
12550 West Frontage Road
Burnsville, MN 55337

Sponsor
Charles D. Caposell
Naval Air Systems Command
AIR-4.5T

Data Item No. 003
Contract Reference Item 0003
Authority - Data Acquisition Documentation No. DI-MGMT-80227
Monthly Report No. 24
Issuing Government Activity
Requiring Office AIR-4.0T

Security Classification - Unclassified

DTIC QUALITY INSPECTED 1

20000418 034

CDRL Distribution List and Addresses

Commander
Naval Air Systems Command
Attn: Mr. Charles Caposell, Code 4.0T
Building 2185, Suite 1190
22347 Cedar Point Rd., Unit 6
Patuxent River, MD 20670-1161

Commander
Naval Air Warfare Center Aircraft Division
Attn: Kathleen Griggs, 4.5.1.3
48110 Shaw Rd.
Building 2187 Unit 5
Patuxent River, MD 20670-0121

Commander, Naval Air Systems Command
Attn: Technical Library, Code AIR-4.0C1
Building 2185
22347 Cedar Point Rd., Unit 6
Patuxent River, MD 20670-1161

Director
Defense Advanced Research Projects Agency / ETO
Attn: E.C. Urban
3701 North Fairfax Dr.
Arlington, VA 22203-1714

Defense Technical Information Center
Attn: DTIC-User Services
8725 Kingman Rd
Fort Belvoir, VA 22060-6218

Additional Distribution List

Henry Girolamo, Program Manager/DARPA Agent
U.S. ARMY SOLDIER SYSTEMS CENTER
Kansas Street - AMSSB-RSS-D (N)
Natick, MA 01760-5020

Mitch Wathen
Office of Special Technology
10530 Riverview Rd.
Fort Washington, MD 20744

1. Progress & Plans

Hardware

Phase 3/4 Boards

The rigid-flex board housing the CPU and display chip sets is being built by the board house. Due to an error they performed in the tooling, the new expected delivery is now in the second week of May.

RF

The Phase 3 Bluetooth radio boards have been verified and are being used for driver and software development. Design on the Phase 4 RF boards will begin in April.

Digianswer has communicated to us that they will have samples of their new Bluetooth PC cards by July. These will be considerably more affordable than their Demo cards, of which we have been using one for development purposes. We hope to be able to obtain the cards earlier than July.

Audio

Andrea Electronics has been working with one of our Phase 2 boards to port their software to our DSP. This work is almost completed. They have received our preliminary design files for the plastic enclosure and are modifying them with suggestions for the mounting of the microphones and speaker to optimize the acoustic performance of the audio module.

Optics

No work was performed on the WID's optics system in the month of March.

Battery System

The development board for the battery system was designed and built. We are in the process of populating it so as to begin testing the Panasonic Li-ion batteries that we are planning to use in the final device.

Mechanical Design

The mechanical design tasks remaining to be completed are:

- On/Off switches mounting in main case
- Completion of light box design
- Mounting of lens and finalization of plastic case
- Audio module case
- RF module case
- Battery case, battery charger, and attachment to battery module on wrist band
- Wrist band clasp

These tasks have been scheduled and are expected to be completed by early June.

Software

Bluetooth Drivers

An early implementation of the WID's display and communication drivers was successfully demonstrated. It broadcasts over our Bluetooth radios either a bouncing ball or a screen capture of whatever is displayed on the host computer.


Work is progressing to render the Bluetooth drivers under Windows CE robust and well engineered. A similar goal is being pursued on the Windows 98, host side.

Audio Drivers

No significant work was done toward an audio driver for CE in the month of March. This is partly due to the fact that we are waiting for Andrea Electronics to finish porting their directional mic array software to our DSP.

High-Level CE Software

No work was done in the month of March on the high-level CE software.

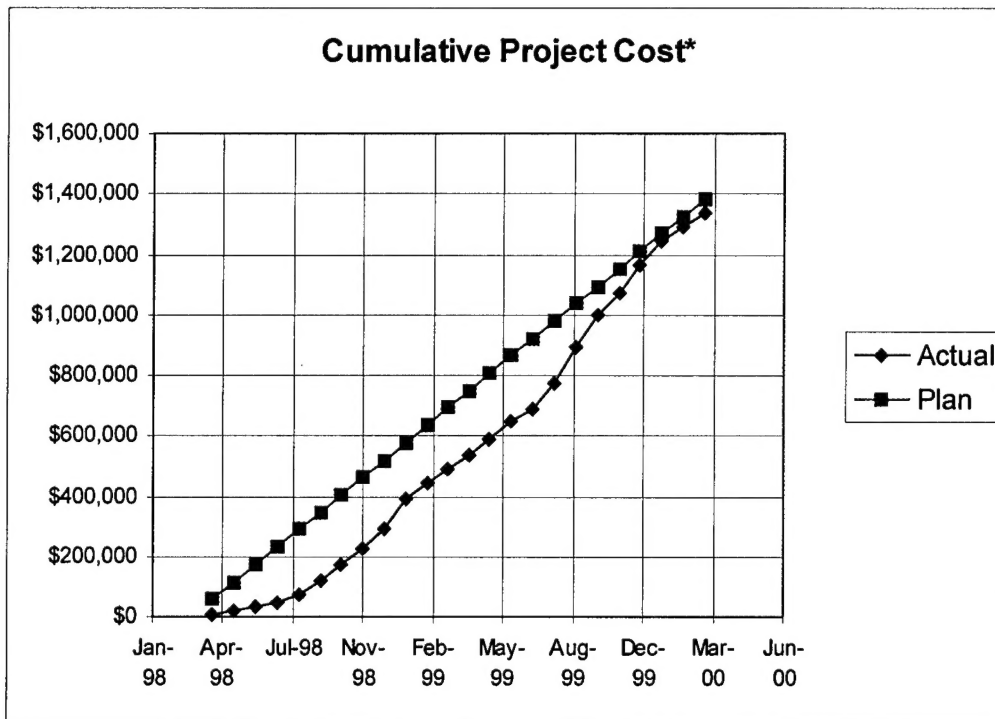

***without G&A and fee**

2. Project Cost

Cost incurred for the period and total cost, without G&A and Fee:

Current Month's Cost*	Cumulative Cost
\$43,603	\$1,333,734

* Current month cost is 1 February through 29 February

Person-hours for the period and cumulatively:

Current Month's Hours	Cumulative Hours
491	16,851

3. Schedule and Staffing

The schedule for the final delivery may have slipped a month due to the following reasons:

- DARPA directed us to suspend work for a couple of weeks in February while the issue of which optics system to use was resolved.
- The board manufacturer made an error in the tooling due to which the main CPU & Display boards will now be delivered in the first half of May. This is two months after the initially expected date for these Phase3 and 4 boards.
- Delivery of Digianswer PC cards is expected in July.

Software work has continued but it will not be possible to complete some porting tasks until the new boards are built and populated. Based on the information available to us now we expect a July delivery.

Staffing has changed somewhat. Bill Meuleners has been moved to another DARPA project, the design of the case for the ViA Motion computer. Therefore, ViA has retained the services of a very senior independent contractor and PE, Bill Siebert, with ten years of specific experience in mechanical design and twenty additional years of experience in electronic and systems design to complete the mechanical design tasks for the WID. We are very excited to have Mr. Siebert working on this project.

The rest of the team is unchanged, except for the fact that the long hardware delivery lead times are allowing us, and in some cases are forcing us, to divide our time between different projects without any additional impact on the WID schedule. It is important to realize that the lower labor hours charged to the project in March and in the coming months are solely due to this fact and not to any decrease in ViA's commitment to complete the WID project as quickly and as thoroughly as promised.

4. Author

Paolo Dini
ViA, Inc.
12550 West Frontage Road
Burnsville, MN 55337

(612) 736-3145
(612) 736-5944 (Fax)
pdini@flexipc.com
